



# Santa Clara Transit Station Project Update

October 5, 2020

#010

## Current Status: Construction

Following Labor Day weekend, the hazardous air quality from the Holiday Farm Fire halted construction at the Santa Clara Transit Station for nearly two weeks. This shut-down has delayed our entire construction schedule; however, we are cautiously optimistic the planned completion date will not be affected.



In September, Delta Construction along with Knife River paved Green Lane, Elementary Lane, and the Park and Ride. Storm water planters and the sidewalk along the north side of Green Lane will be completed in October.

During the latter part of September, the masons were on site and completed the brick exterior walls of the driver relief building.


## Traffic Impacts

Potential intermittent lane closures along River Road and Green Lane.

## Project Overview

In 2015, LTD purchased an 8-acre undeveloped parcel along River Road between Hunsaker Lane and Green Lane to pursue the design and construction of the Santa Clara Transit Station. This site was selected because the property allows for flexible development of a transit station and Park & Ride. The site provides sufficient space to allow for maximum maneuverability of buses and for better access for riders, pedestrians, cyclists, and people who use mobility devices. The design includes 6 bus bays, 55 parking spaces at the adjacent Park & Ride, on-street parking, secure bike parking, covered station platforms, and a small driver relief building.

## Project Funding

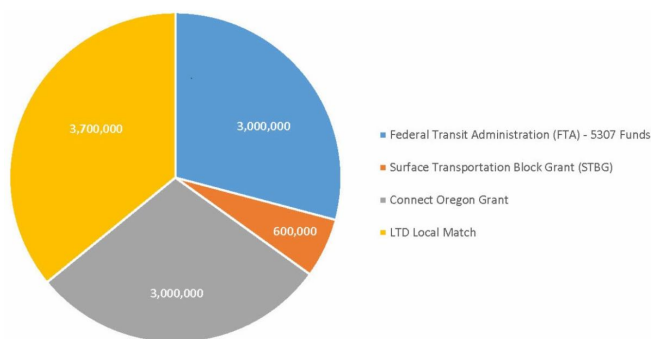

## Information

For More Information: Randi Staudinger, LTD Project Manager, [Randi.Staudinger@LTD.org](mailto:Randi.Staudinger@LTD.org)

For Public Comment: [SCTransit@LTD.org](mailto:SCTransit@LTD.org) or 541-682-3240

